APPLICATION BRIEF / CUSTOMER-CONFIRMED

Tube handling — feeder to assembly

Northline Integration · example company / Confirmed Nov 4, 2026

HANDLING OBJECTIVE

Move two sizes of soft tubes from a feeder, up an incline, and deliver them individually to an assembly station.

Infeed / source **Customer feeder**	Receiving process **Assembly station**
Handling object **Soft elastomer tubes in two variants. Protect the surface and keep each tube separate.**	Surface constraint **Avoid marking or pinching the soft tube surface**

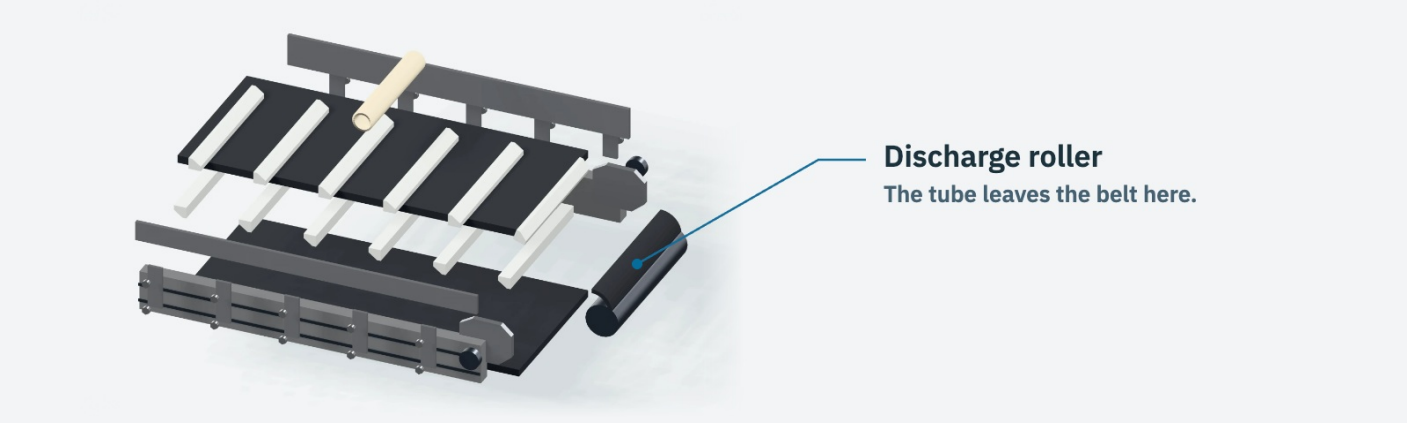


Fig. 01 Discharge assembly from the illustrative tube-transfer model. Reference geometry only.

CUSTOMER RESPONSE · R2

Discharge connection / Customer

Who supplies the transition between the 1450 mm discharge and the proposed 1520 mm receiving station?

NEXT DISCUSSION

Interface ownership

Agree who supplies controls and integration.

APPLICATION BRIEF / ENGINEERING RECORD

Requirements & responsibilities

Part dimensions

Variant	Outside diameter	Length
Tube A	12 mm	160 mm
Tube B	16 mm	240 mm

Movement & constraints

Infeed height
850 mm

Discharge height
1450 mm

Receiving station height
1520 mm

Height difference (receiving minus discharge)
+70 mm

Requested delivery rate
20 parts/min

Delivery
One tube at a time

Accumulation
Not requested

Orientation
Maintain tube orientation at discharge

Available space
Available footprint to be confirmed with a layout drawing

Operating environment
Indoor assembly area

Requested interface responsibilities

Supports
Customer

Infeed connection
Customer

Discharge connection
Customer

Controls and integration
MK to discuss

Project & contact

Contact
Alex Morgan

Organization
Northline Integration · example company

Email
alex@example.com

Location
Connecticut, USA

Requested timing
Planning for the next production phase; date to discuss

Additional notes
This is an illustrative request. No equipment selection, capacity or delivery date has been confirmed.
